
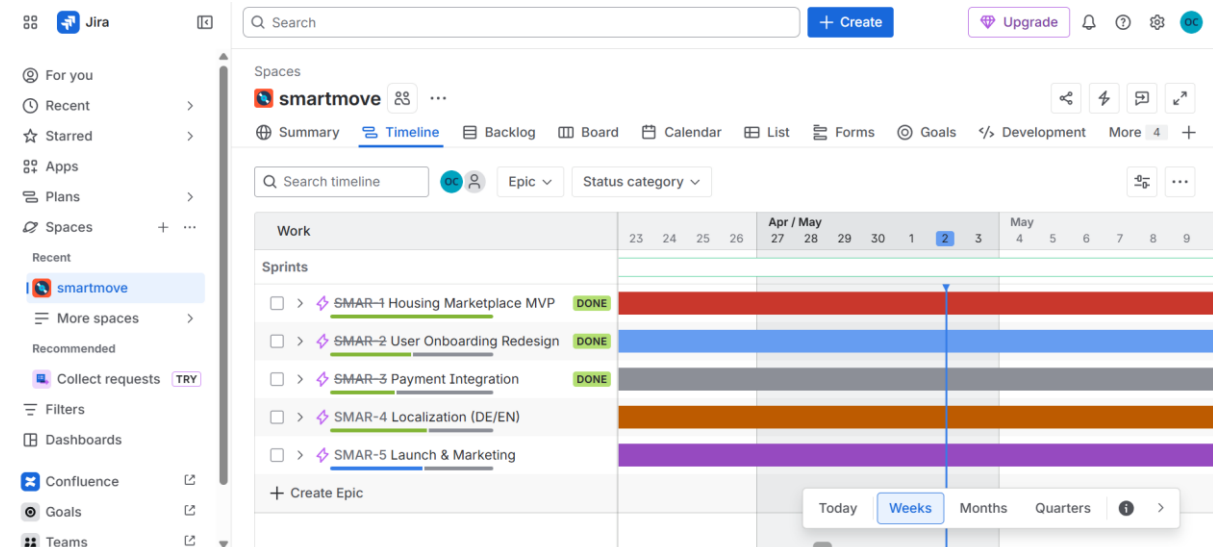


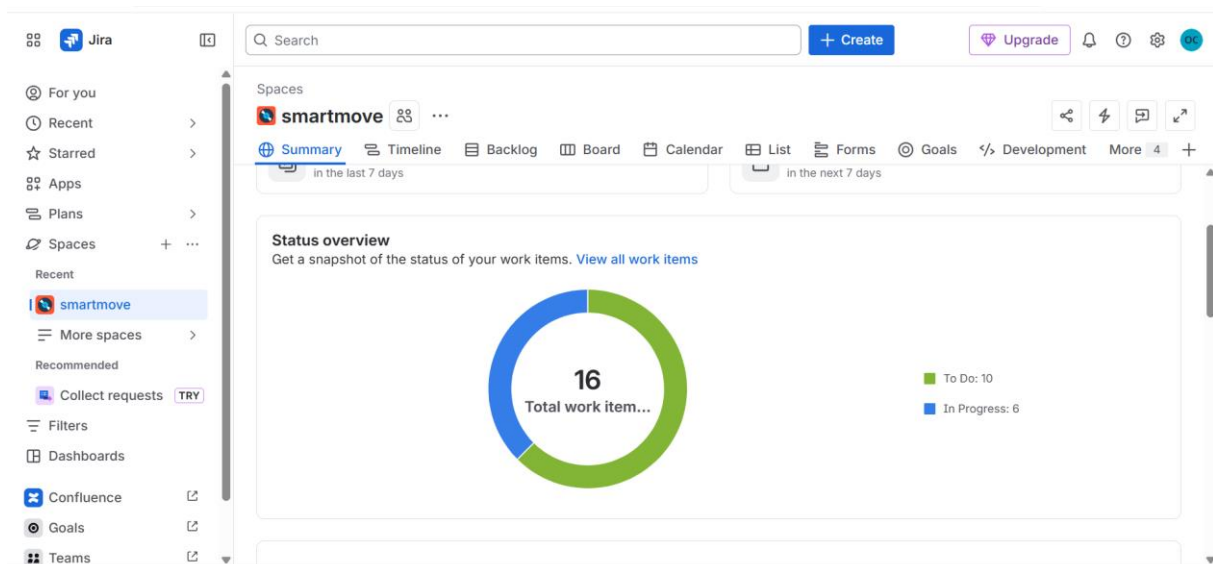

Jira

Search

+ Create

Upgrade

Spaces

smartmove

Summary Timeline Backlog Board Calendar List Forms Goals Development More 4 +

Search backlog

Filter

SMAR Sprint 4	Add dates	(14 work items)	38	15	0	Start sprint	
SMAR-26	App Store listing (DE & EN)	LAUNCH & MARKETING	IN PROGRESS	3			
SMAR-27	Press release for Austrian tech media	LAUNCH & MARKETING	IN PROGRESS	2			
SMAR-28	Social media launch campaign	LAUNCH & MARKETING	IN PROGRESS	2			
SMAR-30	End-to-end regression testing	LAUNCH & MARKETING	IN PROGRESS	8			
SMAR-14	Welcome tour for new users	USER ONBOARDING R...	TO DO	3			
SMAR-15	Email verification flow	USER ONBOARDING R...	TO DO	2			
SMAR-17	Secure deposit payment flow	PAYMENT INTEGRATI...	TO DO	8			
SMAR-19	Refund processing workflow	PAYMENT INTEGRATI...	TO DO	5			

Jira

For you

Recent

Starred

Apps

Plans

Spaces

Recent

smartmove

More spaces

Recommended

Collect requests

Filters

Dashboards

Confluence

Goals

Teams

Search

Create

Upgrade

Spaces

smartmove

Summary

Timeline

Backlog

Board

Calendar

List

Forms

Goals

Development

More

Search backlog

Filter

SMAR-30

End-to-end regression testing

LAUNCH & MARKETING

IN PROGRESS

8

SMAR-14

Welcome tour for new users

USER ONBOARDING R...

TO DO

3

SMAR-15

Email verification flow

USER ONBOARDING R...

TO DO

2

SMAR-17

Secure deposit payment flow

User Onboarding Redesign

TO DO

8

SMAR-19

Refund processing workflow

PAYMENT INTEGRATI...

TO DO

5

SMAR-20

Payment UI — card input form

PAYMENT INTEGRATI...

TO DO

3

SMAR-21

i18n framework setup

LOCALIZATION (DE/EN)

TO DO

5

SMAR-23

Language toggle in settings

LOCALIZATION (DE/EN)

TO DO

2

SMAR-29

Landing page update for V2.0

LAUNCH & MARKETING

TO DO

3

Overview

Date	May 15, 2026
Facilitator	oluchi ohanado(project coordinator)
Participants	Anna Berger, Markus Hofer, Lena Gruber, Stefan Pichler, Julia Eder, Thomas Bauer

Confluence

Ohanado Cindy

Getting started...

Explore Conflu...

Untitled live do...

Retrospective: ...

IT HELP DESK ...

Create

Company hub

Jira

Teams

More

Search

Create

Upgrade

Retrospective: SMAR Sprint 1

Edited Apr 18

Share

Retrospective

What went well

What didn't go well

Strong team collaboration on the marketplace feature. Anna and Markus worked closely on frontend-backend integration for the listing creation flow. Having daily 15-minute syncs between them prevented blockers early.

Apple developer account delay cost us 2 days. Markus was blocked on the Social Login story because our Apple Developer account credentials weren't set up. We should have this ready before sprint start for future integrations.

e.g., Sharing progress at daily standups

↑ Back to top

- Getting started...
- Explore Conflu...
- Untitled live do...
- Retrospective: ...
- IT HELP DESK ...

+ Create

Company hub

Jira

Teams

More

Invite people

+ ⋮

What went well

blockers early.

Onboarding redesign exceeded expectations.

Lena's 3-step signup prototype was ready by day 3, giving the team extra time to polish the welcome tour. User testing with 5 internal testers showed a 40% faster signup time compared to V1.

Early backlog refinement paid off. Because we spent time writing clear acceptance criteria before the sprint

What didn't go well

for future integrations.

API refactoring mid-sprint.

The listing creation endpoint needed restructuring on day 4 when we realized the original design wouldn't support photo uploads efficiently. This added 1 day of unplanned work for Markus.

QA involvement came too late.

Julia wasn't actively involved until the last 2 days. Earlier QA enqaqement would have
